Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
IH-69 Two-Way HOV		827		02-Jan-23 A	04-Jun-26	0
Project Management		762		01-Mar-23 A	04-Jun-26	0
416465.2280	Planning and Feasibility / PE summary	85	0%	01-Mar-23 A	02-Oct-24	0
416465.2270	Project Management	85	0%	01-Mar-23 A	04-Jun-26	0
416465.10010	FY23	0	0%		30-Sep-23*	979
416465.10030	Project Management - FY24	252	0%	02-Oct-23	27-Sep-24	425
416465.10070	Designer Selection	80	0%	11-Jun-24	02-Oct-24	0
416465.10020	FY24	0	0%			13
416465.10040	Project Management - FY24 to Project Finish	424	0%	0		0
416465.10050	Project Complete	0	0%		04-Jun-26*	0
Project Initiation		65		01-Mar-23 A	30-Jun-23	125
416465.1010	Project Strategy	43	48.84%	01-Mar-23 A	30-Jun-23	125
416465.1020	HOV/HOT strategy	65	66.15%	01-Mar-23 A	30-Jun-23	125
416465.1030	TxDOT concurrence on strategy	43	48.84%	01-Mar-23 A	30-Jun-23	125
Operational Analysis / Planning		65		01-Mar-23 A	30-Jun-23	0
416465.1540	Operational Analysis and Planning	65	66.15%	01-Mar-23 A	30-Jun-23	0
Categorical Exclusion		305		02-Jan-23 A	10-May-24	522
416465.2030	Existing Conditions	85	0%	01-Jun-23	29-Sep-23	0
416465.2020	FTA NEPA - CE Concunrrence	20	0%	01-Aug-23	28-Aug-23	130
416465.2120	Inter Agency Meetings	0	0%	13-Sep-23		204
416465.2040	Impact Assessment	62	0%	02-Oct-23	29-Dec-23	0
416465.2130	Inter Agency Meetings	0	0%	14-Dec-23		204
416465.2050	CE Documentation (Draft Document)	52	0%	15-Dec-23	29-Feb-24	0
416465.2060	METRO Review	21	0%	01-Mar-24	29-Mar-24	0
416465.2070	Submit Draft CE to FTA	0	0%		10-May-24	0
Project Description		33		14-Jun-23	31-Jul-23	130
416465.2000	Concurren	33	0%	14-Jun-23	31-Jul-23	130
416465.2010	Detailed pr	33	0%	14-Jun-23	31-Jul-23	130
Public Involvement		158		15-Aug-23	29-Mar-24	130
416465.2080	Public Involvement	158	0%	15-Aug-23	29-Mar-24	130
416465.2090	Project Introduction Meeting	0	0%	13-Sep-23		204
416465.2100	Project Development Meeting	0	0%	14-Dec-23		204
Agency Coordination & Meetings		212		02-Jan-23 A	29-Mar-24	552
416465.2110	Agency Coordination & Meetings	212	0.94%	02-Jan-23 A	29-Mar-24	130
416465.2250	Inter Agency Meeting	0	0%	13-Sep-23		626
416465.2260	Inter Agency Meeting	0	0%	14-Dec-23		626
Concept Development		65		01-Jun-23	31-Aug-23	275
416465.2140	Conceptual Development	63	0%	01-Jun-23	29-Aug-23	275
416465.2150	IAJR	2	0%	30-Aug-23	31-Aug-23	275
TxDOT		827		02-Jan-23 A	04-Jun-26	0

change to 7/14/ 2023A

this task duplicates 416465.2020. suggest deleting or it needs to have the same dates.

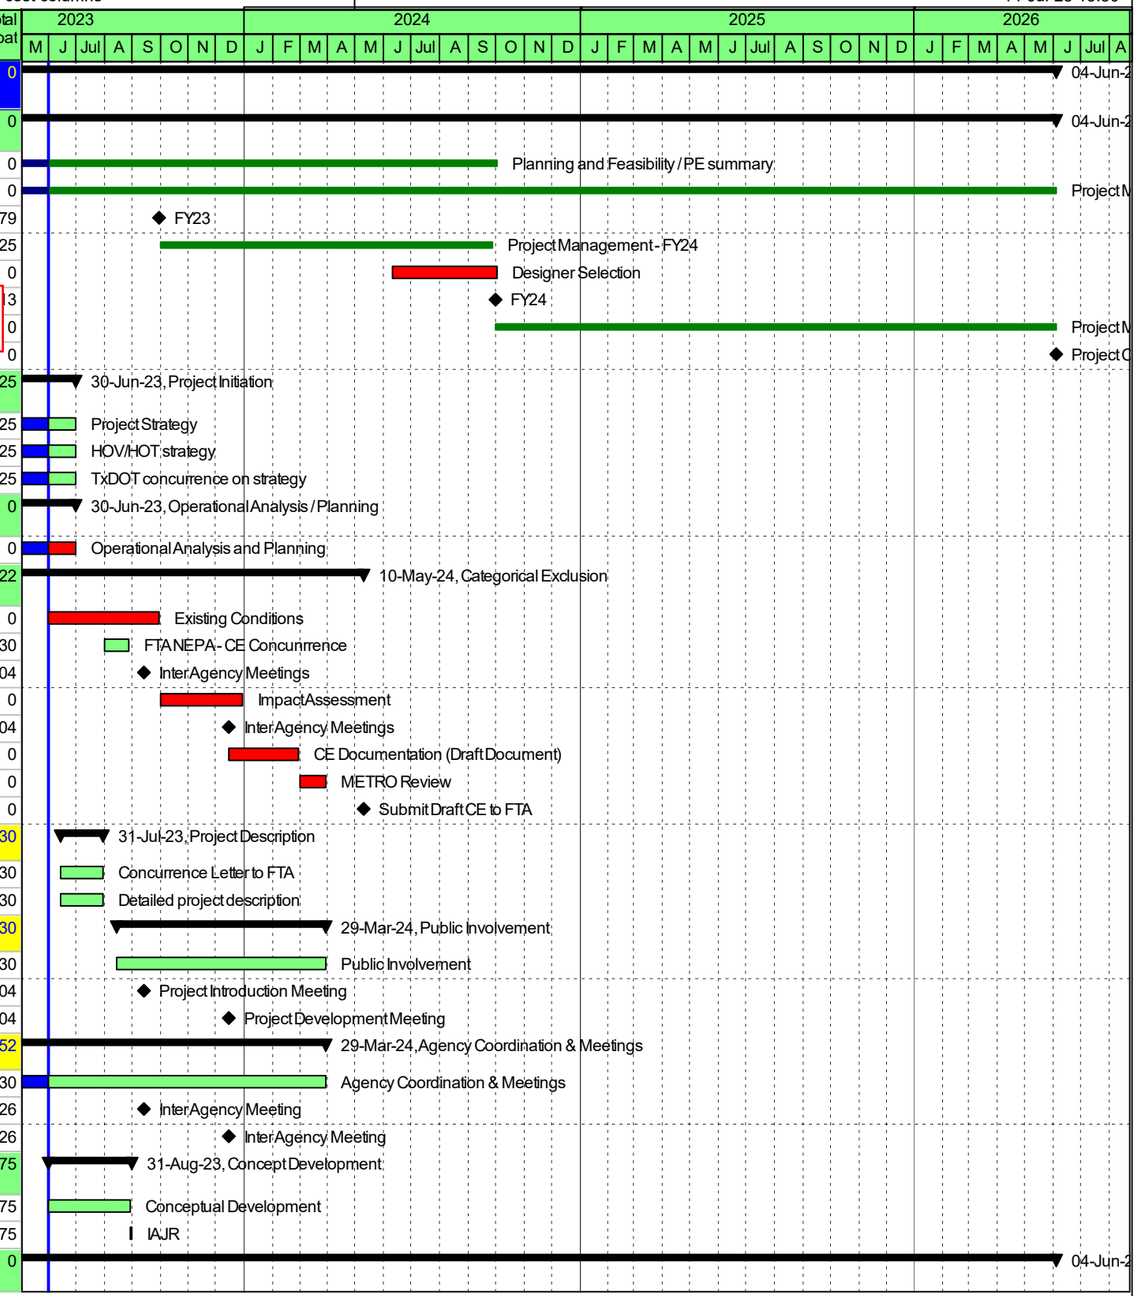

Remaining Level of Effort | Remaining Work
Actual Level of Effort | Critical Remaining Work
Actual Work | ◆ Milestone

IH-69 Two-Way HOV

TASK filter: Remaining Activities (%<>100).
Project ID: **IH-69-A-001**
Data Date: **01-Jun-23**

METRO

Activity ID	Activity Name	Original Duration	Activity % Complete	Start	Finish	Total Float
NHHIP Segment 3A (IH-69 + Spur)		787		02-Jan-23 A	08-Apr-26	40
416465.2160	Design 90%	212	40.09%	02-Jan-23 A	30-Nov-23	212
416465.2170	Design 95%	41	0%	01-Dec-23	31-Jan-24	212
416465.2180	Construction Letting	86	0%	03-Oct-24	06-Feb-25	40
416465.2190	Construction	296	0%	07-Feb-25	08-Apr-26	40
IH-69 Two-Way HOV Project		422		03-Oct-24	04-Jun-26	0
416465.10060	Payment Milestone #1 to TxDOT (Design)	0	0%	03-Oct-24		40
416465.2200	Final Design (Spur to WLUTC)	151	0%	03-Oct-24	08-May-25	0
416465.2210	Construction Letting	62	0%	11-Mar-25	05-Jun-25	0
416465.10080	Payment Milestone #2 to TxDOT (Constructionn)	0	0%	06-Jun-25		252
416465.2220	Construction (Upto Edloe)	252	0%	06-Jun-25	04-Jun-26	0
Public Involvement		421		03-Oct-24	03-Jun-26	1
416465.2230	Public Involvement	421	0%	03-Oct-24	03-Jun-26	1
Agency Coordination & Meetings		610		02-Jan-23 A	29-Jan-26	89
416465.2240	Agency Coordination & Meetings	610	0%	02-Jan-23 A	29-Jan-26	89

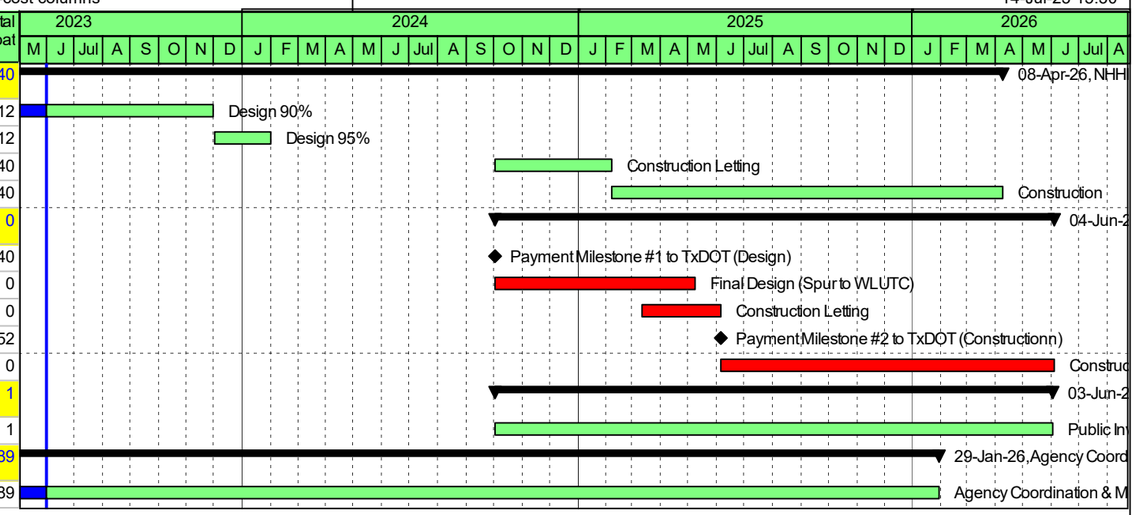

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

IH-69 Two-Way HOV

TASK filter: Remaining Activities (%<>100).
Project ID: **IH-69-A-001**
Data Date: **01-Jun-23**
